NORTH STAR · 1 OF 2

One cockpit where the Technology Command Center commands the fleet of business services by error budget, not by ticket queue

Every service on one screen

Twenty business services ranked by how fast each is burning its error budget, with the regulator's view of impact beside it.

Impact decides who reaches the bridge


Tickets are admitted by business impact; the noise is held below the line where the commander can still see it.

The regulator's three clocks run live

Notify within 1 hour, recover within 4, report within 14 days — counting down beside every incident, from detection to debrief.

BRIDGE seconds
MISSION minutes
DEBRIEF days


Three layers, one record: every command, approval and attestation is written once and kept for seven years.

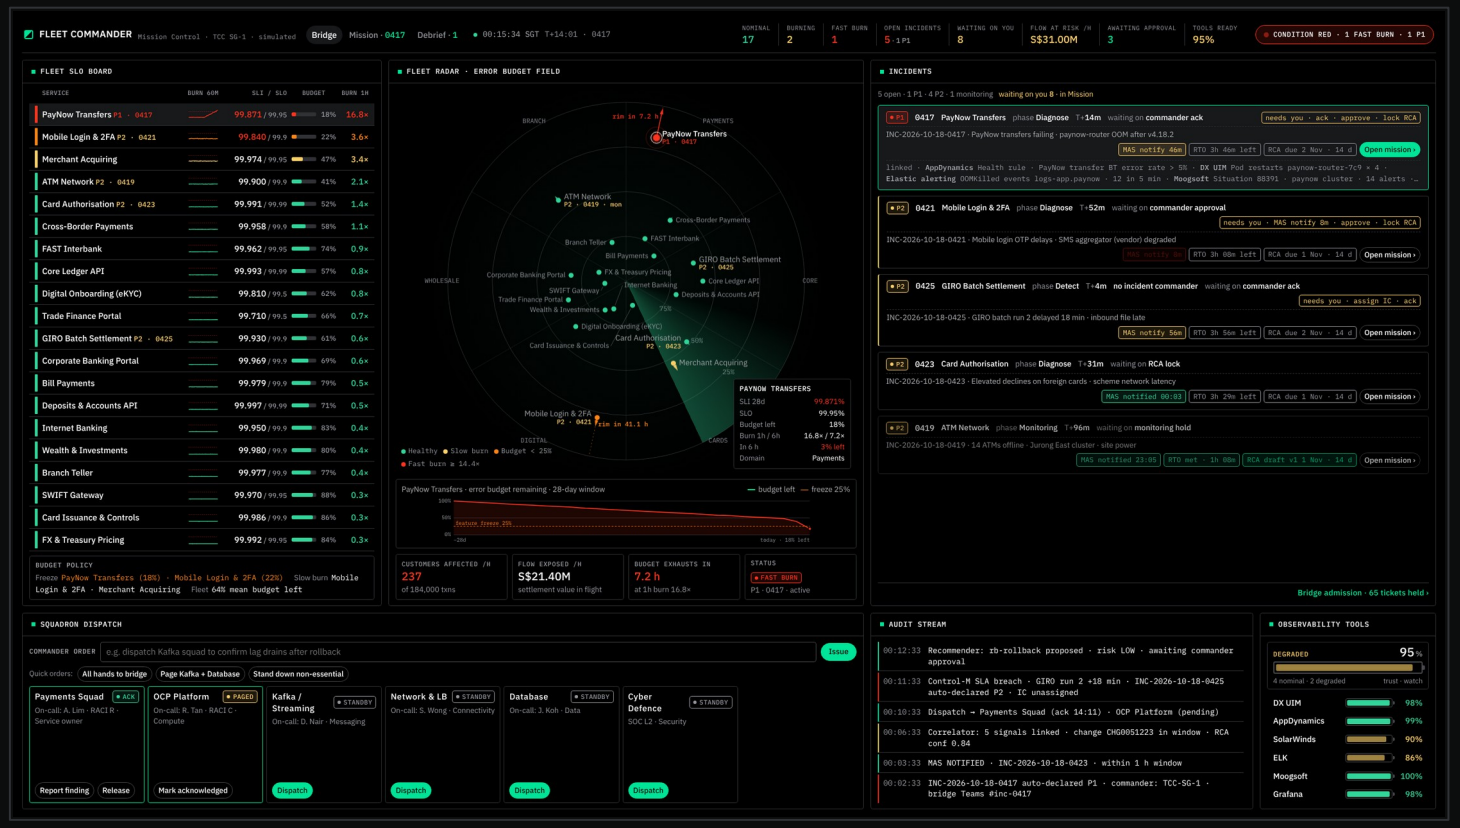

The Bridge — fleet SLO board, error-budget radar, ranked incidents with bridge admission, squadron dispatch, audit stream

NORTH STAR · 2 OF 2

Three layers, three clocks: the Bridge watches in seconds, a Mission runs in minutes, the Debrief settles in days

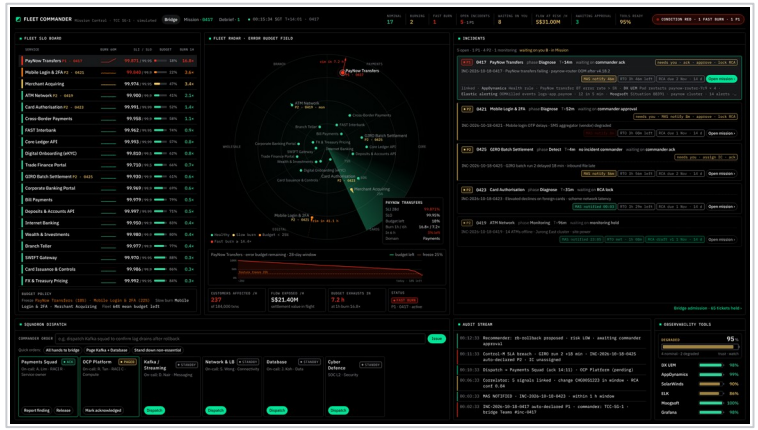

01 BRIDGE · SECONDS


Fleet awareness

Fleet Commander — the TCC shift lead

"Where do I spend my attention right now?"

- Fleet SLO board — twenty services ranked by burn
- Error-budget radar with six-hour projections
- Incidents admitted by impact; squadrons dispatched

Ticket queue → **error-budget priority**

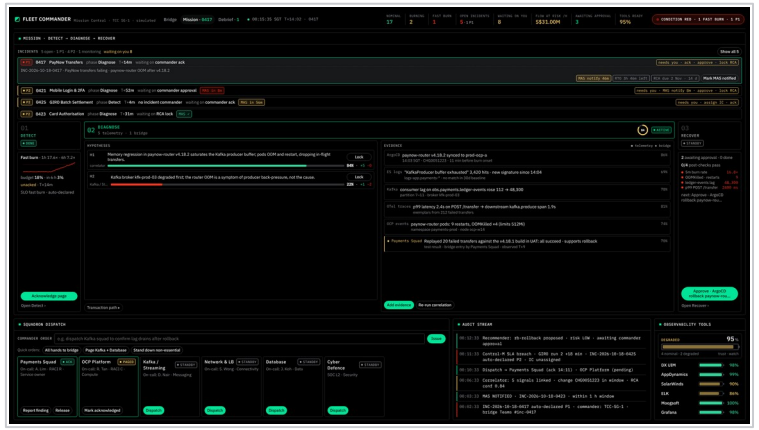

02 MISSION · MINUTES


One incident, commanded

Incident Commander with the SME squads

"What is broken, why, and what do we do — safely?"

- Detect → Diagnose → Recover, one phase in focus
- Evidence and hypotheses to a locked root cause
- Signed runbooks · four-eyes · every step audited

Bridge call from memory → **commanded mission with an audit trail**

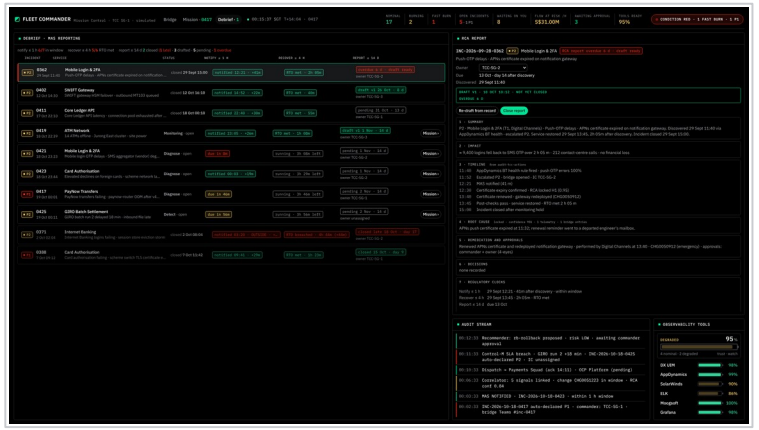

03 DEBRIEF · DAYS

Obligations settled

Incident Commander with Risk & Compliance

"Did we meet our obligations — and can we prove it?"

- Notify ≤ 1 h · recover ≤ 4 h · report ≤ 14 d
- RCA report assembled from the record, not retyped
- Closed when settled; proof kept for seven years

Report written after the fact → **report assembled from the record**

We are at the start: the tools exist and the cockpit is a working prototype, but fleet SLOs and the command plane do not yet exist

Three steps from here, each ending in a demo to this forum and a stop / continue gate.

YOU ARE HERE

0 · TODAY Q4 2026

Tools in production. Cockpit prototype on simulated data. Incidents worked from the ticket queue.

1 · INSTRUMENT H1 2027

SLIs and error budgets for Tier-1 services. Burn-rate alerting pages. The Bridge live in the TCC.

2 · COMMAND H2 2027

Mission live: correlation, evidence, locked RCA. Pre-approved runbooks run through EDA under four-eyes.

3 · ASSURE 2028

Debrief live: MAS clocks, RCA from the record, seven-year audit stream. All tiers on the Bridge.

In place today

- ELK, Grafana, AppDynamics, DX UIM, SolarWinds and Moogsoft in production — the sensors and the correlator
- Event-driven Ansible proven end to end; alert-as-code schema and RACI routing designed; Backstage IDP in use
- Fleet Commander prototype: three pages, twenty services, admission gate, MAS clocks — a decision on what to build, not a sketch

Not yet

- No fleet-wide SLOs or error budgets; no SLI store, so burn rate is not computed anywhere
- Incident handling is ticket-driven — ServiceNow first, business impact second; no signed runbook catalogue or automation governance
- No incident-record contract between ServiceNow and a cockpit; the prototype runs on simulated telemetry, not production feeds

WHAT THE PLATFORM TEAM NEEDS

To build it, the platform team needs a dedicated squad, protected time and three decisions from this table

People — a squad of six for 24 months

- Six full-time: an SRE product lead, two SLI/SLO engineers (Elastic transforms, OpenTelemetry), a front-end engineer (React, Canvas), an automation engineer (EDA, Ansible, ArgoCD) and a data and platform engineer (Elasticsearch, Kafka)
- Part-time: a Risk & Compliance liaison, a ServiceNow engineer, and a UX designer for the first two quarters

Time — ring-fenced from BAU

- The six are off the on-call rota and BAU queues for the first four quarters
- A TCC commander seconded one day a week as product owner
- Quarterly demo to this forum with a stop / continue gate at each one


Budget — sized in the Q4 2026 business case

- Elasticsearch capacity for the SLI store and the seven-year audit stream (hot 30 d → cold)
- OpenShift / ECK capacity for the SLI aggregation service
- Vendor API enablement (AppDynamics, Moogsoft, DX UIM, SolarWinds), TCC wall display, SLO training

Decisions — three we need now

- Every Tier-1 service has a named owner and an agreed SLO by the end of Q1 2027
- Pre-approved runbooks in a signed catalogue may execute under four-eyes without a per-run CAB; freeze windows still hard-block
- ServiceNow remains the incident record of truth, with a published contract to the cockpit (INC, CHG, PRB, IC assignment)

The solution is a command plane on top of the tools we already run: nothing is replaced, and every action takes the same governed path

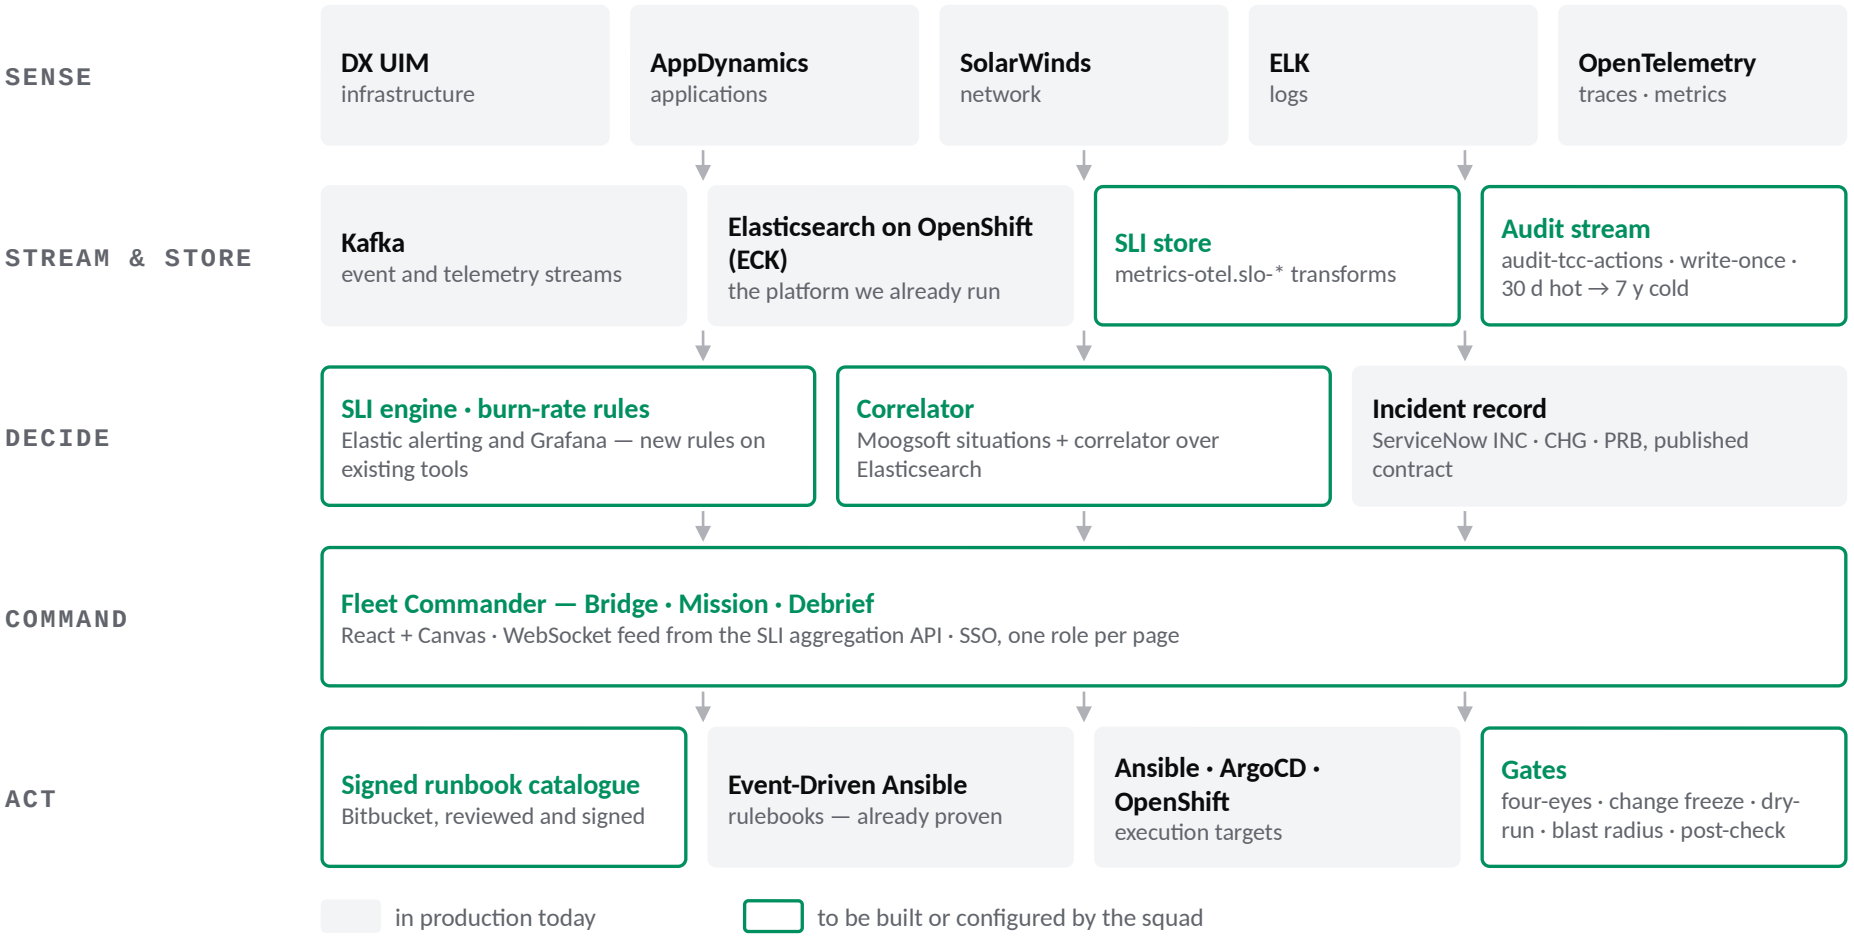

MAS TRM CONTROLS

- Approval recorded with reason, RCA confidence and change reference
- Second approver is the service owner; break-glass actions retro-approved
- Notify ≤ 1 h · recover ≤ 4 h · report ≤ 14 d, timed from discovery
- Evidence, hypotheses, outcomes and attestations append-only
- Every step in the audit stream, retained seven years

THE NEXT TWO YEARS · Q4 2026 → Q4 2028

Tier-1 services are on the Bridge within a year; the full command-and-assurance loop is live by the end of 2028

